


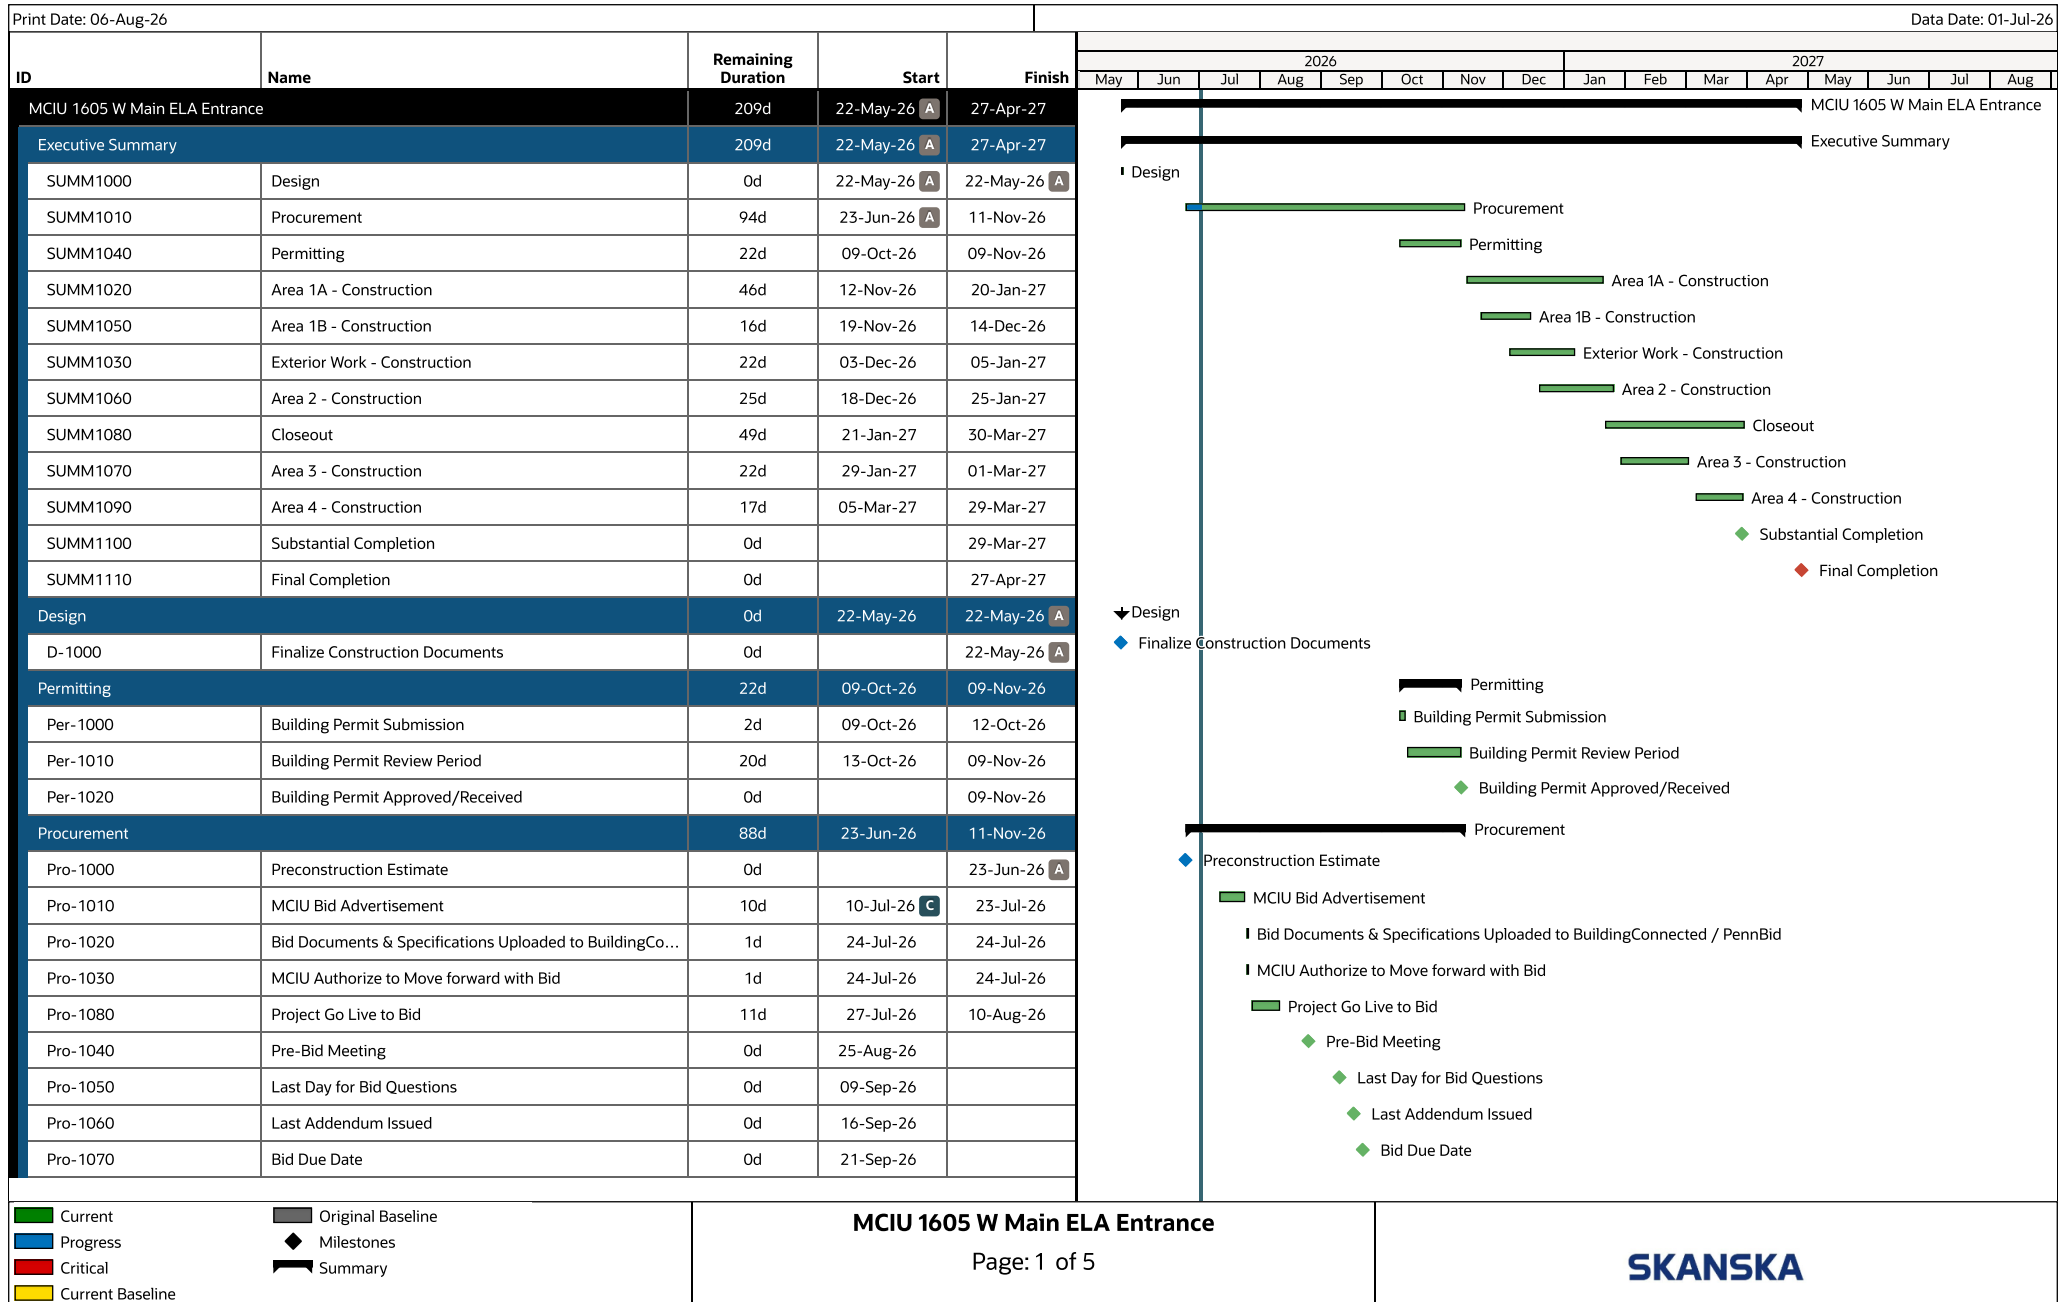


https://primavera-us2.oraclecloud.com/web/p/schedule_activity?ctx=484019&app=schedule_management&selectedItem=43475080_ACTIVITY 2/5

https://primavera-us2.oraclecloud.com/web/p/schedule_activity?ctx=484019&app=schedule_management&selectedItem=43475080_ACTIVITY 3/5

Print Date: 06-Aug-26					Data Date: 01-Jul-26																			
ID	Name	Remaining Duration	Start	Finish	2026												2027							
					May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug				
1B-1100	Re-Set Classroom Furniture (By Owner)	1d	15-Dec-26	15-Dec-26	I Re-Set Classroom Furniture (By Owner)																			
Area 2		25d	18-Dec-26	25-Jan-27	I Area 2																			
2-1010	Safe Off Existing Electric	1d	18-Dec-26	18-Dec-26	I Safe Off Existing Electric																			
2-1000	Remove Wall Base & Wainscoting & Trim	1d	19-Dec-26	19-Dec-26	I Remove Wall Base & Wainscoting & Trim																			
2-1020	Remove Existing Flooring	1d	19-Dec-26	19-Dec-26	I Remove Existing Flooring																			
2-1030	Prep Framing for New Drywall	1d	20-Dec-26	20-Dec-26	I Prep Framing for New Drywall																			
2-1040	Electrical RI	1d	26-Dec-26	26-Dec-26	I Electrical RI																			
2-1050	New Drywall Hand & Finish	3d	27-Dec-26	03-Jan-27	I New Drywall Hand & Finish																			
2-1060	Ceiling Adjustment	1d	08-Jan-27	08-Jan-27	I Ceiling Adjustment																			
2-1120	Clean and Prep for Monday School	1d	09-Jan-27	09-Jan-27	I Clean and Prep for Monday School																			
2-1070	Prime & 1st Coat Paint	2d	10-Jan-27	15-Jan-27	I Prime & 1st Coat Paint																			
2-1080	Electric Finish	2d	16-Jan-27	17-Jan-27	I Electric Finish																			
2-1090	2nd Coat Paint	1d	22-Jan-27	22-Jan-27	I 2nd Coat Paint																			
2-1100	New Flooring & Base	2d	23-Jan-27	24-Jan-27	I New Flooring & Base																			
2-1110	Re-Set Classroom Furniture (By Owner)	1d	25-Jan-27	25-Jan-27	I Re-Set Classroom Furniture (By Owner)																			
Area 3		22d	29-Jan-27	01-Mar-27	I Area 3																			
3-1000	Safe Off Existing Electric	1d	29-Jan-27	29-Jan-27	I Safe Off Existing Electric																			
3-1010	Remove Wall Base & Wainscoting & Trim	1d	29-Jan-27	29-Jan-27	I Remove Wall Base & Wainscoting & Trim																			
3-1020	Remove Existing Flooring	1d	29-Jan-27	29-Jan-27	I Remove Existing Flooring																			
3-1030	Prep Framing for New Drywall	1d	30-Jan-27	30-Jan-27	I Prep Framing for New Drywall																			
3-1040	Electrical RI	1d	31-Jan-27	31-Jan-27	I Electrical RI																			
3-1050	New Drywall Hand & Finish	4d	05-Feb-27	12-Feb-27	I New Drywall Hand & Finish																			
3-1060	Prime & 1st Coat Paint	1d	13-Feb-27	13-Feb-27	I Prime & 1st Coat Paint																			
3-1110	Clean and Prep for Monday School	1d	14-Feb-27	14-Feb-27	I Clean and Prep for Monday School																			
3-1070	Electric Finish	1d	19-Feb-27	19-Feb-27	I Electric Finish																			
3-1080	2nd Coat Paint	1d	20-Feb-27	20-Feb-27	I 2nd Coat Paint																			
3-1090	New Flooring & Base	2d	21-Feb-27	26-Feb-27	I New Flooring & Base																			
3-1100	Re-Set Classroom Furniture (By Owner)	1d	01-Mar-27	01-Mar-27	I Re-Set Classroom Furniture (By Owner)																			
Area 4		17d	05-Mar-27	29-Mar-27	I Area 4																			
4-1000	Remove Wall Base & Partition & Trim	1d	05-Mar-27	05-Mar-27	I Remove Wall Base & Partition & Trim																			
Current Progress Critical Current Baseline Original Baseline Milestones Summary					MCIU 1605 W Main ELA Entrance																			
					Page: 4 of 5																			
					SKANSKA																			

Print Date: 06-Aug-26					Data Date: 01-Jul-26																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
ID	Name	Remaining Duration	Start	Finish	2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
					May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
4-1010	Safe Off Existing Electric	1d	05-Mar-27	05-Mar-27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														</

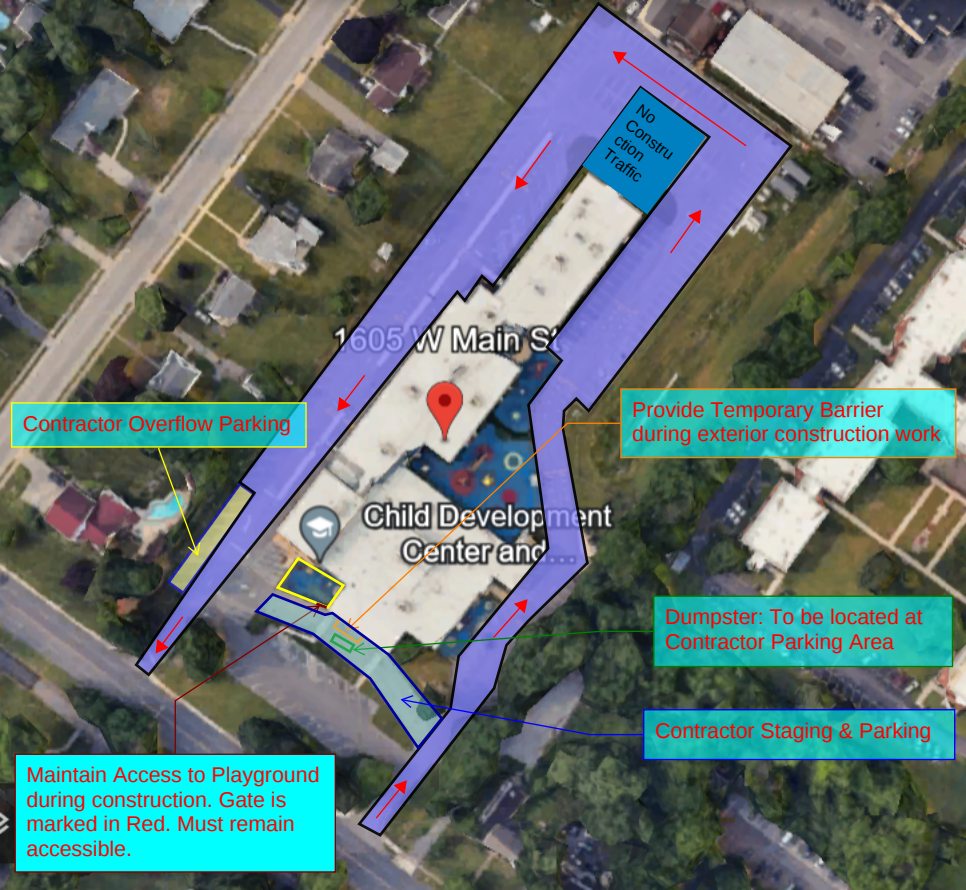

Contractor Overflow Parking

Provide Temporary Barrier during exterior construction work


Dumpster: To be located at Contractor Parking Area

Contractor Staging & Parking


Maintain Access to Playground during construction. Gate is marked in Red. Must remain accessible.

5/12/2025 6:03:39 PM

2 1ST FLOOR PARTIAL DEMO RCP AREA (A)
1/4" = 1'-0"

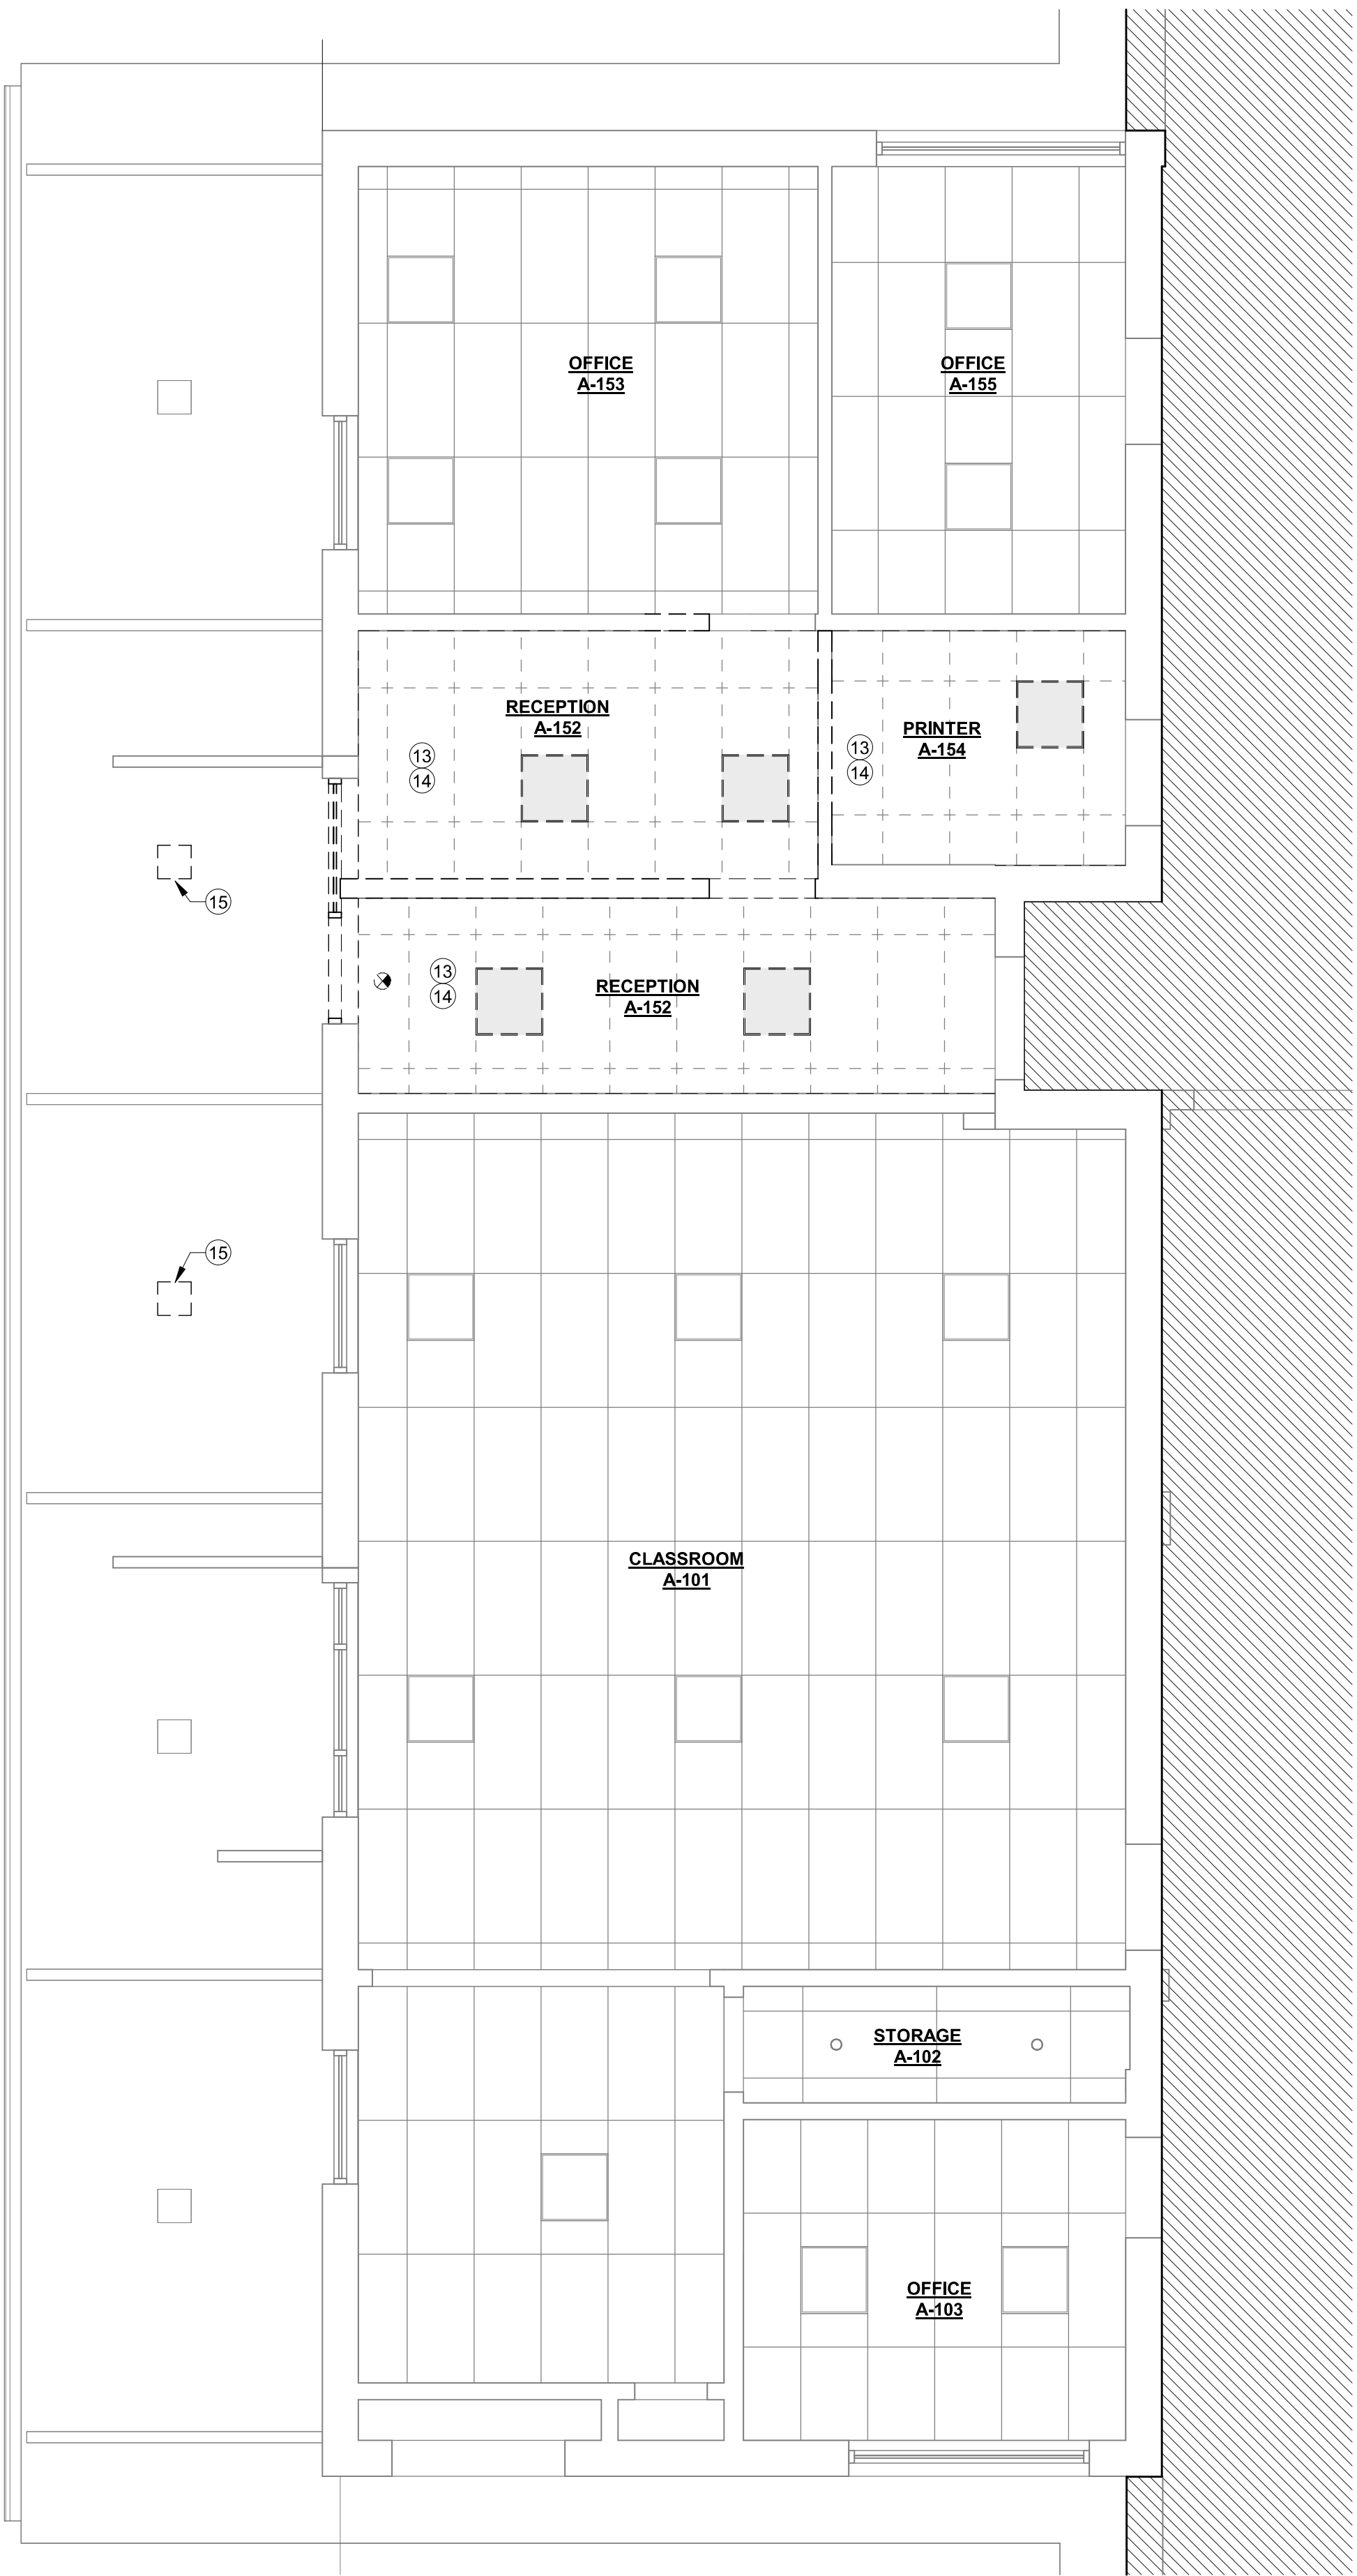

1 1ST FLOOR DEMOLITION PARTIAL PLAN AREA (A)
1/4" = 1'-0"

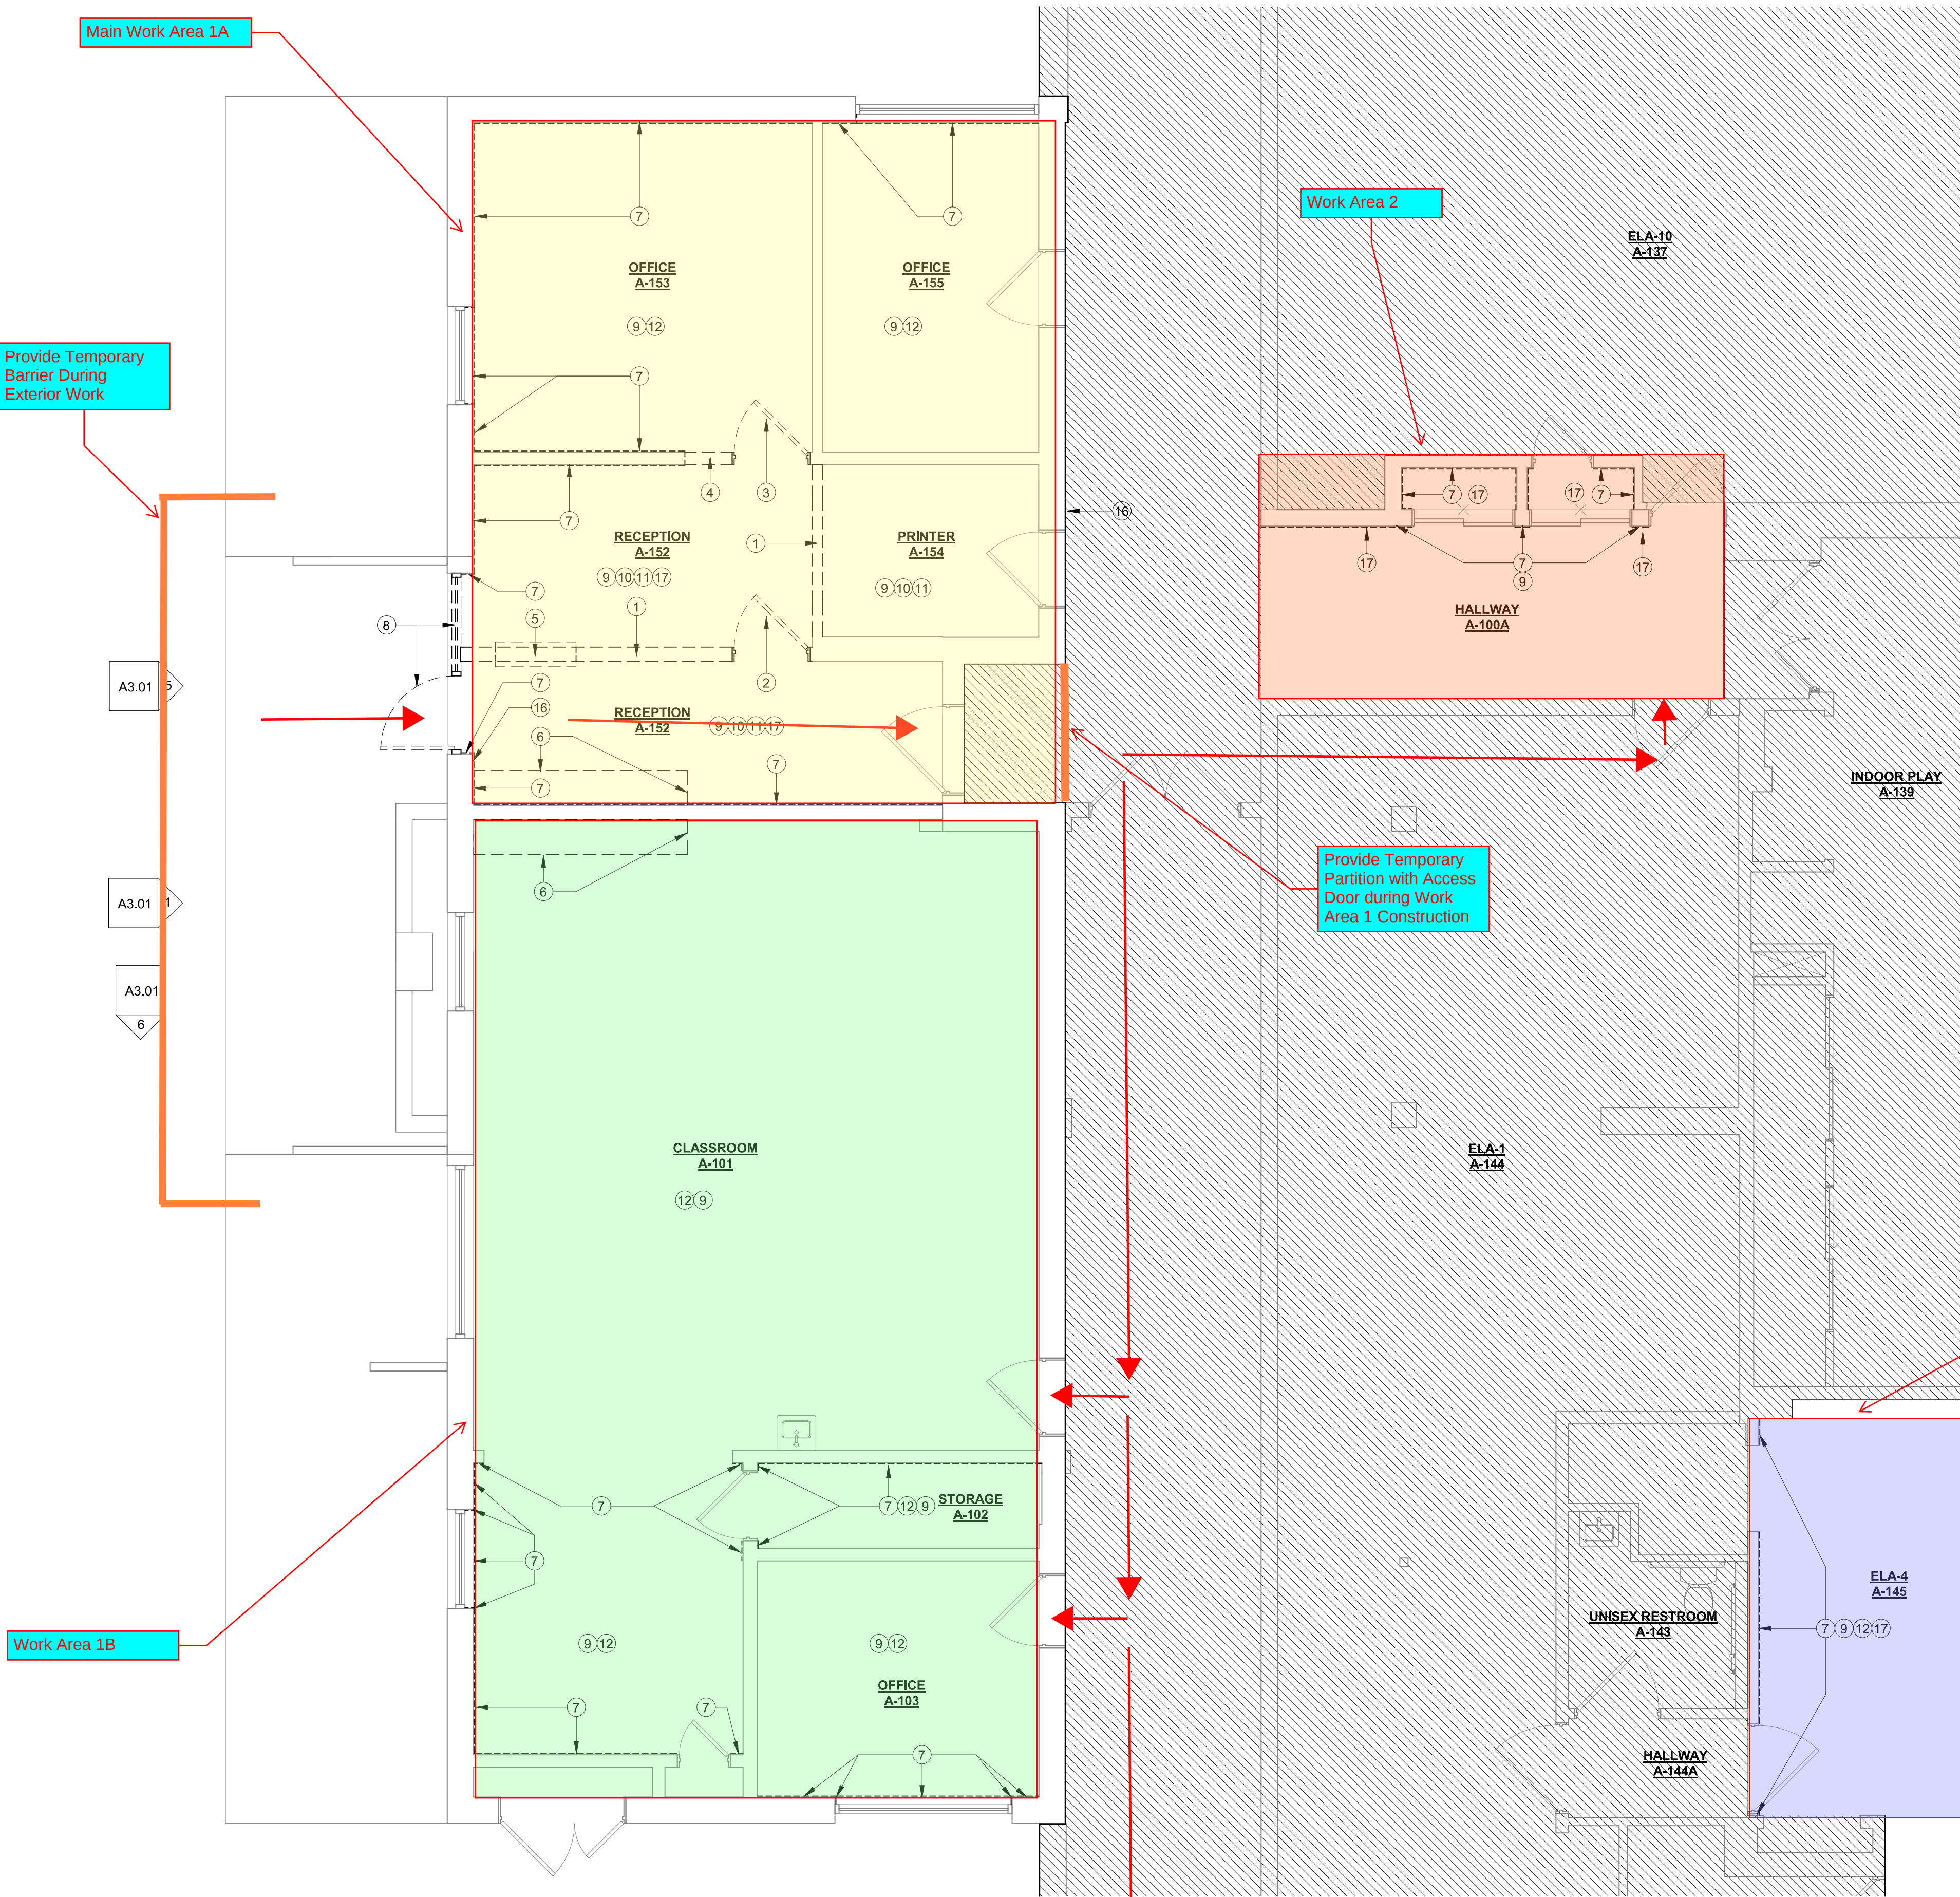

DEMOLITION GENERAL NOTES

- DEMOLITION IS NOT NECESSARILY LIMITED TO WHAT IS SHOWN ON DRAWINGS. THE INTENT IS TO INDICATE THE GENERAL SCOPE OF DEMOLITION REQUIRED TO COMPLETE THE WORK IN ACCORDANCE WITH THE CONTRACT DRAWINGS. AS REQUIRED, PATCH & REPAIR ALL EXISTING SURFACES WHERE EQUIPMENT HAS BEEN REMOVED EITHER BY CONTRACTOR OR BY OTHERS, OR AS A RESULT OF DEMOLITION OF ADJACENT & ATTACHED CONSTRUCTION. PATCHING IS TO BE SMOOTH AND LEVEL WITH ADJACENT SURFACES TO REMAIN. PATCH TO MATCH SAME CONSTRUCTION AS ADJACENT SURFACES.
- AS APPLICABLE, REMOVE ALL ABANDONED & NO LONGER ACTIVE WIRING & CABLING FROM EITHER THE CEILING PLENUM OR DEMOLISHED PARTITIONS. INACTIVE CIRCUITS TO BE REMOVED BACK TO THE CIRCUIT PANEL. DATA CABLING BACK TO THE SOURCE & TELEPHONE CABLING BACK TO THE PUNCH-DOWN BLOCKS, WHERE NOTED, REMOVE AND CAP OFF EXISTING PLUMBING AS REQUIRED PER CODE.
- AS REQUIRED, ANY DISRUPTED FIREPROOFING OF ALL BUILDING STRUCTURAL MEMBERS & WITHIN WALLS, FLOORS & CEILINGS SHALL BE SUPPLEMENTED AFTER DEMOLITION, IN ACCORDANCE WITH ALL CURRENT APPLICABLE CODES, REGULATIONS & ORDINANCES OF ALL GOVERNING BODIES HAVING JURISDICTION OVER THE PROJECT.
- REFER TO ELECTRICAL DRAWINGS FOR REMOVAL OF OUTLETS, SWITCHES, FACEPLATES, COVER PLATES, AND WALL HUNG ITEMS ON EXISTING WALLS TO REMAIN AND FOR LOCATION OF NEW DEVICES.
- THE CONTRACTOR IS REQUIRED TO MAINTAIN OPERATION OF BUILDING AND LIFE SAFETY SYSTEMS IN OCCUPIED AREAS DURING CONSTRUCTION. CLEAR & UNOBSTRUCTED PATHS ARE TO BE MAINTAINED TO EGRESS EXITS DURING CONSTRUCTION.
- EXISTING FLOORING SUBSTRATE TO BE PREPARED FOR NEW FLOORING SURFACES. PREPARATION TO INCLUDE REMOVAL OF GLUE RESIDUE, TACK STRIPS, AND ASSOCIATED ITEMS TO PROVIDE A SMOOTH AND LEVEL SURFACE FOR NEW FLOORING MATERIALS.
- REMOVE EXISTING LIGHT FIXTURES WHERE NOTED ON DEMOLITION PLANS.
- COORDINATE WITH MEPF DRAWINGS FOR DEMO SCOPE OF WORK OF EXISTING MECHANICAL, PLUMBING, ELECTRICAL, FIRE ALARM AND WIRELESS ACCESS POINTS.

DEMO PLAN LEGEND

- EXISTING WALL TO REMAIN
- EXISTING CONSTR. TO BE REMOVED
- EXISTING DOOR TO REMAIN
- EXISTING DOOR TO BE REMOVED
- NOT IN PROJECT SCOPE
- EXISTING RECESSED 2X4 CEILING FIXTURE TO BE REMOVED

RCP DEMO LEGEND

- EXISTING ACT CEILING TO REMAIN
- EXISTING ACT CEILING TO BE REMOVED

DEMOLITION KEYED NOTES

- CONTRACTOR TO REMOVE EXISTING INTERIOR PARTITION, PROTECT AND REPAIR AS REQUIRED EXISTING WALLS AND FLOOR UNDERLAYMENT TO REMAIN. PROVIDE INFILL AS REQUIRED.
- CONTRACTOR TO REMOVE EXISTING INTERIOR DOOR AND FRAME, PROTECT AND REPAIR AS REQUIRED EXISTING WALLS TO REMAIN.
- EXISTING DOOR, FRAME AND HARDWARE TO BE RELOCATED, REFER TO NEW WORK PLANS FOR NEW LOCATION.
- CONTRACTOR TO REMOVE PORTION OF EXISTING WALL TO PREPARE FOR NEW DOOR OPENING. EXISTING DOOR TO BE RELOCATED TO NEW OPENING. REFER TO NEW WORK PLANS FOR LOCATION.
- CONTRACTOR TO REMOVE EXISTING CHECKIN PASS THRU WINDOW AND FRAME IN ENTIRETY.
- CONTRACTOR TO REMOVE EXISTING FLOWER POT WALL IN ENTIRETY. PROTECT AND REPAIR AS REQUIRED EXISTING WALLS AND FLOORS TO REMAIN. COORDINATE WITH NEW WORK PLANS FOR NEW FINISHES.
- CONTRACTOR TO REMOVE EXISTING WAINSCOTING, TRIM AND WALL BASE IN ENTIRETY. PROTECT AND REPAIR AS REQUIRED EXISTING WALLS, FLOORS WINDOW SILLS AND EXTERIOR WALL CAVITY TO REMAIN. COORDINATE WITH NEW WORK PLANS FOR NEW FINISHES AND DETAILS.
- CONTRACTOR TO REMOVE EXISTING EXTERIOR STOREFRONT IN ENTIRETY. PROTECT AND REPAIR AS REQUIRED EXISTING WALLS, FLOOR SLAB AND STEEL BEAM HEADER TO REMAIN. COORDINATE WITH NEW WORK PLANS, ELEVATIONS AND DETAILS FOR NEW FINISHES.
- REFER TO ELECTRICAL DRAWINGS FOR REMOVAL OF EXISTING POWER DATA, OUTLETS AND LIGHT SWITCHES ON WALLS.
- CONTRACTOR TO REMOVE EXISTING FLOORING, INCLUDING ANY UNDERLAYMENT/ADHESIVE. PREP FOR NEW FLOORING INSTALLATION. SEE NEW WORK PLANS FOR NEW FLOORING TYPE AND LOCATIONS.
- CONTRACTOR TO REMOVE AND PROTECT EXISTING FURNITURE AND EQUIPMENT THROUGHOUT ROOM. CONTRACTOR TO CONFIRM WITH THE OWNER WHAT ITEMS NEED TO BE SALVAGED FOR DELIVERY TO THE OWNER.
- CONTRACTOR TO PROTECT EXISTING FURNITURE EQUIPMENT, AND WALL MOUNTED MATERIALS TO REMAIN DURING DEMOLITION.
- CONTRACTOR TO DEMO EXISTING CEILING GRID AND CEILING TILE. PREP AREA TO RECEIVE NEW FINISHES. CONTRACTOR TO DEMO ALL EXISTING LIGHT FIXTURES AND EXIT SIGN. REFER TO ELECTRICAL DRAWINGS FOR ADDITIONAL INFORMATION.
- REFER TO ELECTRICAL, MECHANICAL AND FIRE PROTECTION DRAWINGS FOR REMOVAL OF MISCELLANEOUS CEILING MOUNTED EQUIPMENT.
- CONTRACTOR TO REMOVE EXISTING EXTERIOR SURFACE MOUNTED LIGHTS. PATCH AND REPAIR AREA TO RECEIVE NEW FINISHES. COORDINATE WITH NEW WORK PLANS FOR NEW LIGHTING.
- CONTRACTOR TO REMOVE EXISTING ROOM SIGNAGE.
- CONTRACTOR TO REMOVE EXISTING WALL BASE AND ANY UNDERLAYMENT/ADHESIVE. PREP FOR NEW WALL BASE INSTALLATION. SEE NEW WORK PLANS FOR NEW WALL BASE TYPE AND LOCATIONS.



Blackney Hayes

phone: (215) 629-0922 ext. 131
Contact Person: TROY HILL

OWNER

MCIU
phone: 610.755.9404
Contact Person: Alfred Howard

MEP

Snyder Hoffman
phone: 610.694.8020
Contact Person: Shane Nipper

Project:

**26-012 MCJU - ELA
ENTRANCE
RENOVATIONS**

Project Address:
1605 W Main St.
Norristown, PA 19403

Sheet Title:

**1ST FLOOR
DEMOLITION PLANS**

Seal

DUTY TO INSPECT CONTRACT DOCUMENTS PRIOR TO STARTING WORK

Any party who relies in part or whole on the content of these Construction Documents shall, before beginning any work, be responsible for fully inspecting the complete set of Contract Documents, including all Drawings, Specifications, and Addenda, for completeness, conflicts, scope of work, and suitability for constructing the building. All parties relying on these documents represent that they have expertise in the area of their responsibility and are knowledgeable regarding industry standards, product requirements and code requirements and therefore are qualified to fully evaluate and interpret the contract documents. All parties relying on these documents must, prior to beginning work, submit all requests for clarifications and additional information to the Architect in writing. All parties who begin work hereby certify that the documents are suitable for their intended purposes unless noted in specific written exception beforehand.

Warning: Actual conditions may vary from conditions shown on this drawing. Confirm all information in the field before proceeding with any work and notify the Architect in writing if a variation is discovered.

This drawing is not to be copied or transmitted in any form without the express written authorization of Blackney Hayes. All ideas and concepts depicted or suggested in this drawing are the property of Blackney Hayes.

Release
Date
Comments

05.01.2026 PROGRESS SET

BH Job Number: 26-012

Scale: As indicated

Drawn By: SW

Checked By:

Approved By:

Sheet No.

AD1.01

© Copyright 2025 Blackney Hayes
