Update 10/22/26

rint Date 19- ct-26 | Data Date: 30 Sep-26

ID	Name	Remaining Duration	Start	Finish
Willow Grove Annex R novation Project		443d	10-Feb-26 A	09-Jun-28
Executive Summary		439d	06-Oct-26	09-Jun-28
PROC1250	Procurement	72d	06-Oct-26	13-Jan-27
PROC1245	Construction Phase	367d	14-Jan-27	09-Jun-28
Milestones		367d	14-Jan-27	09-Jun-28
MS1000	Project Award	0d	14-Jan-27	
MS1001	NTP	0d	14-Jan-27	
MS1005	Structure Complete	0d		01-Sep-27
MS1002	Foundation Start	0d	02-Sep-27	
MS1004	Structure Start	0d	02-Sep-27	
MS1012	Start Fitout	0d	09-Sep-27	
MS1006	Facade Start	0d	30-Sep-27	
MS1008	Roof Complete	0d		10-Nov-27
MS1007	Facade Complete	0d		22-Dec-27
MS1009	Weather Tight	0d		22-Dec-27
MS1003	Foundation Complete	0d		22-Dec-27
MS1010	Perm Power	0d		05-Jan-28
MS1011	Conditioned Air Availible	0d	06-Jan-28	
MS1013	Start Drywall	0d	20-Jan-28	
MS1014	Start Ceiling Grid	0d	08-Feb-28	
MS1018	Elevators Complete (State Inspection)	0d		01-Mar-28
MS1015	Start Flooring	0d	11-Apr-28	
MS1016	Start Punchlist	0d	09-May-28	
MS1017	Substantial Completion	0d		17-May-28
MS1019	Final Completion	0d		09-Jun-28
Design, Permitting & Procurement		131d	10-Feb-26 A	31-Mar-27
Design		4d	17-Jun-26 A	05- ct-26
Construction Document Phase		4d	18-Sep-26 A	05- ct-26
PROC1295	Bid Package Prep 2	4d	18-Sep-26 A	05- ct-26
IBC 2021 Addendum		0d	17-Jun-26 A	30-Sep-26



Current
Progress
Critical
Current Baseline
riginal Baseline
Milestones
Summary


illow Grove Annex Renovation Project

Page: 1 of 6

SKANSKA

Print Date: 19-Oct-26 | Data Date: 30-Sep-26

ID	Name	Remaining Duration	Start	Finish
IBC1002	Addendum Permit Review	0d	17-Jun-26 A	30-Sep-26
Land Entitlements & Permitting		33d	10-Feb-26 A	13-Nov-26
PROC1218	Building Permit - Submit & Approve	33d	10-Feb-26 A	13-Nov-26
Utility Coordination		20d	04-Mar-27	31-Mar-27
Gas		20d	04-Mar-27	31-Mar-27
UTL-1000	PECO - Install Gas Service	15d	04-Mar-27	24-Mar-27
UTL-1001	PECO - Install Gas Meter	5d	25-Mar-27	31-Mar-27
Electric		5d	04-Mar-27	10-Mar-27
UTL-1002	Utility Disconnect	5d	04-Mar-27	10-Mar-27
Procurement		72d	06-Oct-26	13-Jan-27
PROC1247	Bid Phase	33d	06-Oct-26	19-Nov-26
PROC1263	Pre-Bid Meeting	0d	13-Oct-26 C	
PROC1300	Last Day for Questions	0d		06-Nov-26 C
PROC1301	Issue Final Bid Addendum	0d		11-Nov-26 C
PROC1248	Bid Review, Descope & Recommend…	12d	20-Nov-26	07-Dec-26
PROC1302	Submit Recommendation to Commi…	7d	08-Dec-26	16-Dec-26
PROC1249	Contract Execution & Approval	20d	17-Dec-26	13-Jan-27
PROC1265	Commissioner Meeting to Approve …	0d	17-Dec-26 C	
Preconstruction		352d	04-Feb-27	09-Jun-28
Renovation and Addition		352d	04-Feb-27	09-Jun-28
CONS1691	Owner Move Out & FFE Relocations	40d	17-Apr-28	09-Jun-28
Submit and Approve		15d	04-Feb-27	24-Feb-27
GC Long Lead (Exterior Skin/Roof/Glazing)		15d	04-Feb-27	24-Feb-27
GCLL-1002	S/A Glazing	15d	04-Feb-27	24-Feb-27
GCLL-1001	S/A Roof	15d	04-Feb-27	24-Feb-27
GCLL-1000	S/A Exterior	15d	04-Feb-27	24-Feb-27
EC Long Lead (Generator/Panel Boards/Gear)		15d	04-Feb-27	24-Feb-27
ECLL-1001	S/A Panel Boards	15d	04-Feb-27	24-Feb-27
ECLL-1002	S/A Gear	15d	04-Feb-27	24-Feb-27
ECLL-1000	S/A Generator	15d	04-Feb-27	24-Feb-27

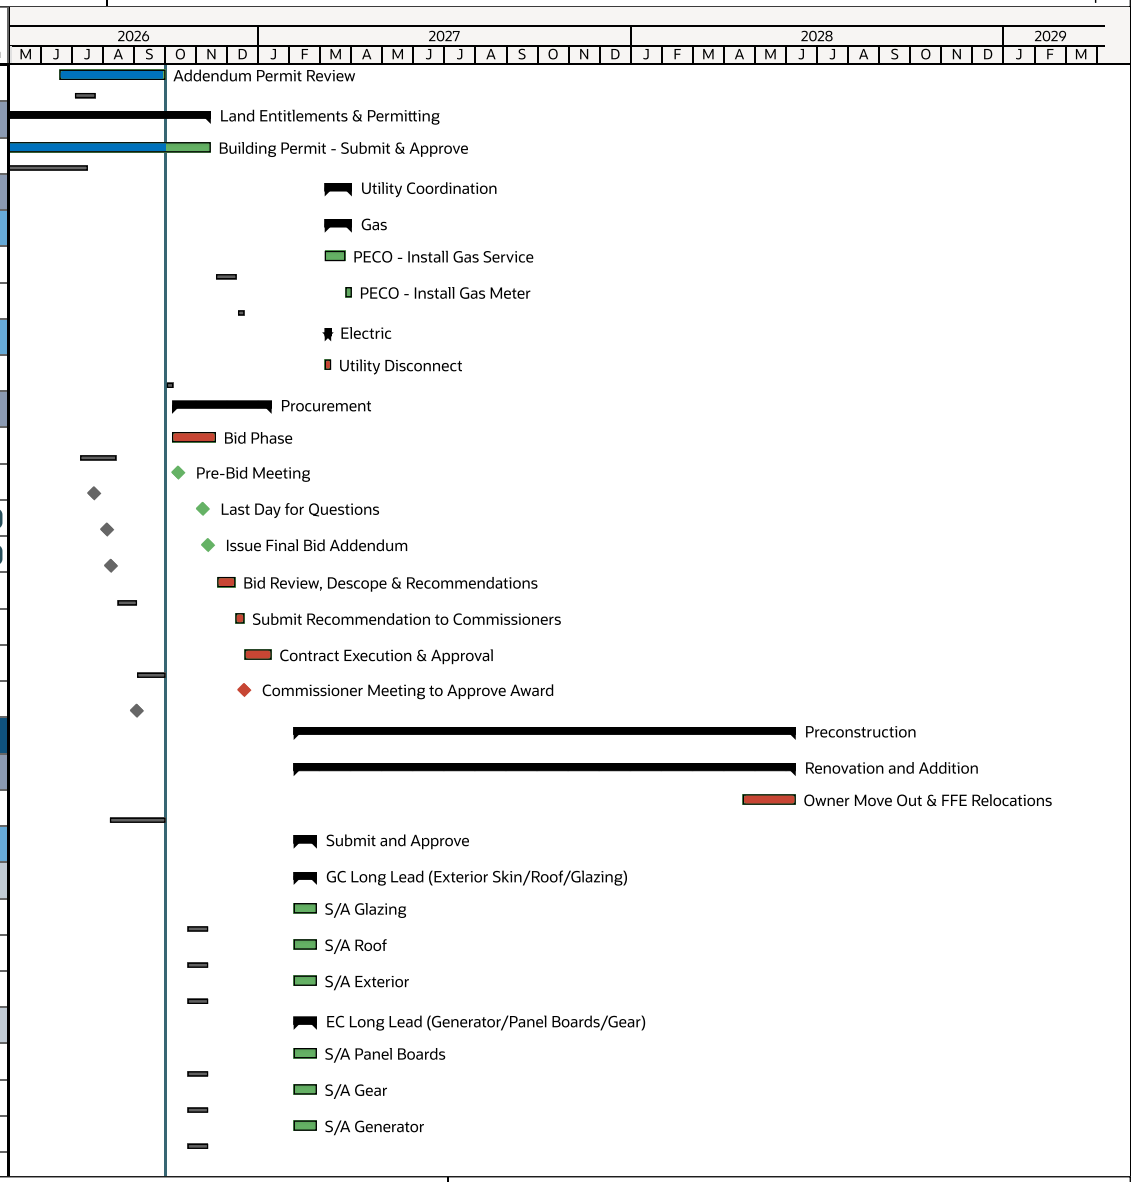

Current
Progress
Critical
Current Baseline
Original Baseline
Milestones
Summary


Willow Grove Annex Renovation Project

SKANSKA

Print Date: 19-Oct-26

Data Date: 30-Sep-26

ID	Name	Remaining Duration	Start	Finish
MC Long Lead (RTU/Above Ceiling Coordination)		15d	04-Feb-27	24-Feb-27
MCLL-1001	S/A Above Ceiling Coordination	15d	04-Feb-27	24-Feb-27
MCLL-1000	S/A RTU	15d	04-Feb-27	24-Feb-27
Fab and Deliver		200d	25-Feb-27	01-Dec-27
GC Long Lead (Exterior Skin/Roof/Glazing)		70d	25-Feb-27	02-Jun-27
GCLL-2000	F/D Exterior	30d	25-Feb-27	07-Apr-27
GCLL-2001	F/D Roof	20d	25-Feb-27	24-Mar-27
GCLL-2002	F/D Glazing	70d	25-Feb-27	02-Jun-27
EC Long Lead (Generator/Panel Boards/Gear)		200d	25-Feb-27	01-Dec-27
ECLL-2000	F/D Generator	125d	25-Feb-27	18-Aug-27
ECLL-2001	F/D Panel Boards	80d	25-Feb-27	16-Jun-27
ECLL-2002	F/D Gear	200d	25-Feb-27	01-Dec-27
MC Long Lead (RTU/Above Ceiling Coordination)		150d	25-Feb-27	22-Sep-27
MCLL-2001	F/D Above Ceiling Coordination	60d	25-Feb-27	19-May-27
MCLL-2000	F/D RTU	150d	25-Feb-27	22-Sep-27
Construction		352d	04-Feb-27	09-Jun-28
Renovation & Addition		352d	04-Feb-27	09-Jun-28
CONS1693	Mobilize & Tempoary Logistics	20d	04-Feb-27	03-Mar-27
CON1-2700	Final Inspections / Completion	5d	05-Jun-28	09-Jun-28
Demolition		130d	04-Mar-27	01-Sep-27
Interior Demo		50d	04-Mar-27	12-May-27
COND-1000	MEP Safe Off	5d	04-Mar-27	10-Mar-27
COND-1010	Interior Demo (Floors 1 - 4)	45d	11-Mar-27	12-May-27
Exterior Demo		95d	22-Apr-27	01-Sep-27
COND-1020	Exterior Demo - North Elevation	20d	22-Apr-27	19-May-27
COND-1021	Exterior Demo - East Elevation	20d	20-May-27	16-Jun-27
COND-1022	Exterior Demo - South Elevation	20d	17-Jun-27	14-Jul-27
COND-1023	Exterior Demo - West Elevation	20d	15-Jul-27	11-Aug-27
COND-1024	Roof Demo	15d	12-Aug-27	01-Sep-27
Structure / Exterior		347d	04-Feb-27	02-Jun-28

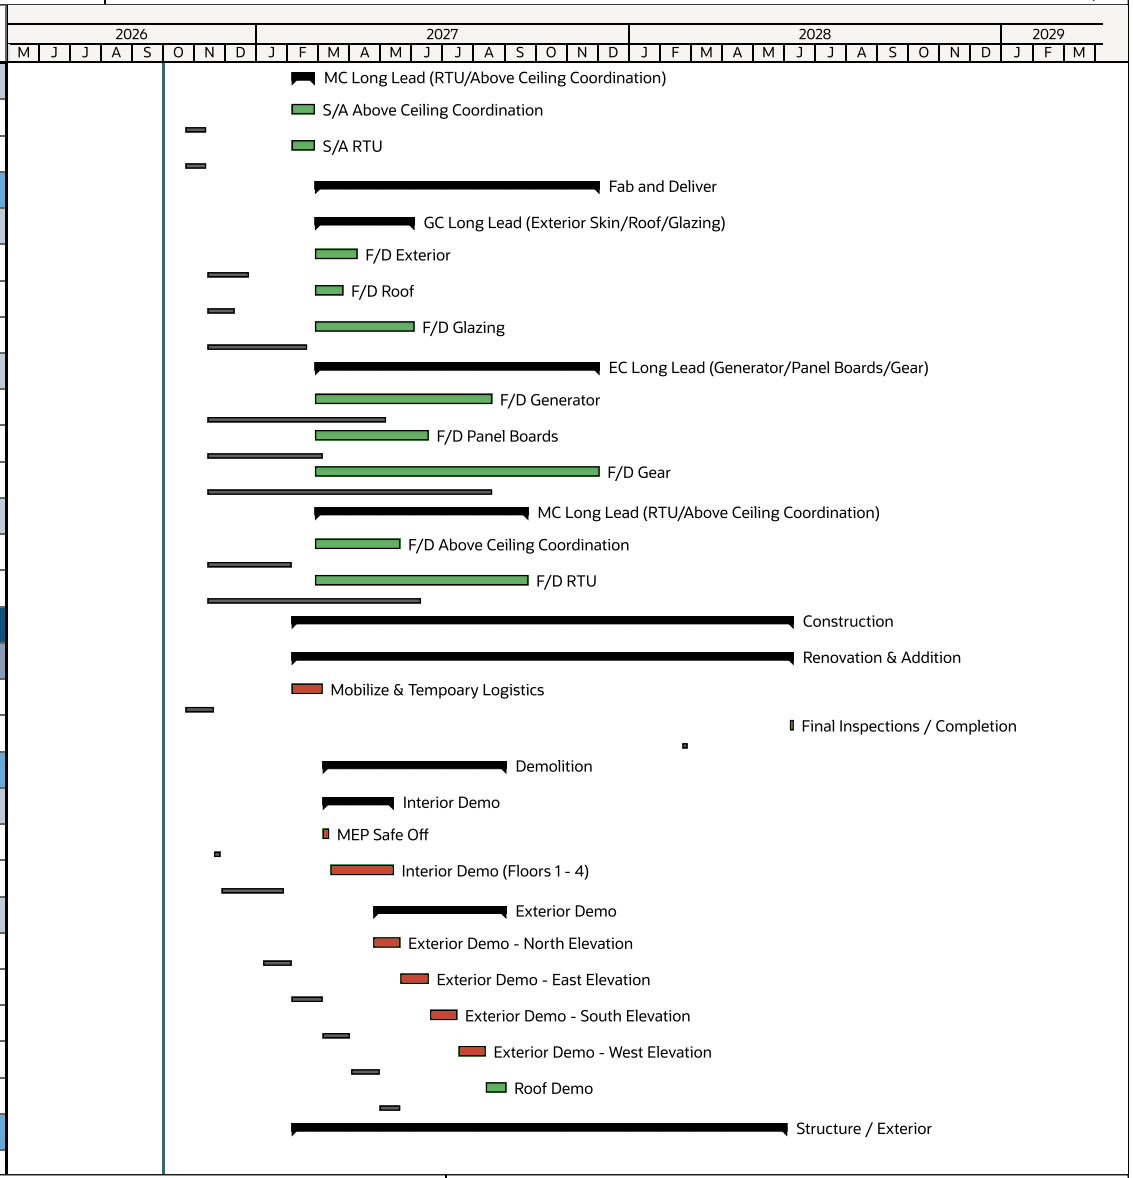

Current
Progress
Critical
Current Baseline
Original Baseline
Milestones
Summary

Willow Grove Annex Renovation Project

SKANSKA

Print Date: 19-Oct-26

Data Date: 30-Sep-26

ID	Name	Remaining Duration	Start	Finish
CONEX-1000	Structural Upgrades/Infill - North Ea…	40d	08-Jul-27	01-Sep-27
CONEX-1010	Install New Enclosure - West Elevation	20d	02-Sep-27	29-Sep-27
CONEX-1020	Install New Enclosure - South Elevati…	20d	30-Sep-27	27-Oct-27
CONEX-1030	Install New Enclosure - North / East	40d	28-Oct-27	22-Dec-27
Roof		105d	02-Sep-27	26-Jan-28
CONR-1402	Screen Wall Structual Connections	15d	02-Sep-27	22-Sep-27
CONR-1000	Temp Utilities/Service	10d	02-Sep-27	15-Sep-27
CONR-1100	Roof Drains & Leaders	20d	16-Sep-27	13-Oct-27
CONR-1200	Roof Dunnage & Curbs	20d	14-Oct-27	10-Nov-27
CONR-1401	Install Membrane	15d	14-Oct-27	03-Nov-27
CONR-1400	Set Roof Top MEP Equipment & Con…	40d	11-Nov-27	05-Jan-28
CONR-1403	Install Screen Wall	15d	06-Jan-28	26-Jan-28
Site		347d	04-Feb-27	02-Jun-28
CONEX-1031	Site Mobilize (Fence, E&S)	10d	04-Feb-27	17-Feb-27
CONEX-1032	Excavate / Install / Backfill Storm	15d	17-Jun-27	07-Jul-27
CONEX-1034	Milling / Paving	10d	24-Apr-28	05-May-28
CONEX-1033	Site Finishes (Striping / Signage / La…	20d	08-May-28	02-Jun-28
Renovation / Fit Out		212d	12-Aug-27	02-Jun-28
Elevator		40d	06-Jan-28	01-Mar-28
CONE-1000	Elevator Demo	20d	06-Jan-28	02-Feb-28
CONE-1001	Elevator Install	20d	03-Feb-28	01-Mar-28
Floor 1		193d	12-Aug-27	08-May-28
CON1-1200	Overhead Rough Ins - Floor 1	20d	12-Aug-27	08-Sep-27
CON1-1400	Interior Framing - Floor 1	15d	09-Sep-27	29-Sep-27
CON1-1500	In Wall Rough In - Floor 1	15d	07-Oct-27	27-Oct-27
CON1-1600	Install Drywall & Finish Partitions - Fl…	20d	23-Dec-27	19-Jan-28
CON1-1800	Prime Coat Walls - Floor 1	10d	20-Jan-28	02-Feb-28
CON1-1900	Install Ceiling Grid - Floor 1	10d	25-Jan-28	07-Feb-28
CON1-2000	Install Ceiling Fixtures - GRD's - Floor 1	15d	01-Feb-28	21-Feb-28
CON1-2200	Finish Paint - Floor 1	10d	03-Feb-28	16-Feb-28



Current
Progress
Critical
Current Baseline
Original Baseline
Milestones
Summary


Willow Grove Annex Renovation Project

SKANSKA

Print Date: 19-Oct-26

Data Date: 30-Sep-26

ID	Name	Remaining Duration	Start	Finish
CON1-2100	Install Millwork & Casework - Floor 1	15d	29-Feb-28	20-Mar-28
CON1-2300	Install MEP Devices & Trim - Floor 1	20d	29-Feb-28	27-Mar-28
CON1-2400	Install Flooring - Floor 1	10d	28-Mar-28	10-Apr-28
CON1-2500	Install Doors & Hardware - Floor 1	10d	11-Apr-28	24-Apr-28
CON1-2600	Final Cleaning & Punchlist - Floor 1	10d	25-Apr-28	08-May-28
Floor 2		177d	09-Sep-27	12-May-28
CON2-1200	Overhead Rough Ins - Floor 2	20d	09-Sep-27	06-Oct-27
CON2-1400	Interior Framing - Floor 2	15d	07-Oct-27	27-Oct-27
CON2-1500	In Wall Rough In - Floor 2	15d	04-Nov-27	24-Nov-27
CON2-1600	Install Drywall & Finish Partitions - Fl...	20d	23-Dec-27	19-Jan-28
CON2-1800	Prime Coat Walls - Floor 2	15d	20-Jan-28	09-Feb-28
CON2-1900	Install Ceiling Grid - Floor 2	15d	25-Jan-28	14-Feb-28
CON2-2000	Install Ceiling Fixtures - GRD's - Floor 2	15d	01-Feb-28	21-Feb-28
CON2-2200	Finish Paint - Floor 2	15d	10-Feb-28	01-Mar-28
CON2-2100	Install Millwork & Casework - Floor 2	15d	29-Feb-28	20-Mar-28
CON2-2300	Install MEP Devices & Trim - Floor 2	20d	02-Mar-28	29-Mar-28
CON2-2400	Install Flooring - Floor 2	10d	30-Mar-28	12-Apr-28
CON2-2500	Install Doors & Hardware - Floor 2	10d	13-Apr-28	26-Apr-28
CON2-2600	Final Cleaning & Punchlist - Floor 2	10d	27-Apr-28	10-May-28
CON2-2700	Final Inspections - Floor 2	2d	11-May-28	12-May-28
Floor 3		157d	07-Oct-27	12-May-28
CON3-1200	Overhead Rough Ins - Floor 3	20d	07-Oct-27	03-Nov-27
CON3-1400	Interior Framing - Floor 3	15d	04-Nov-27	24-Nov-27
CON3-1500	In Wall Rough In - Floor 3	15d	02-Dec-27	22-Dec-27
CON3-1600	Install Drywall & Finish Partitions - Fl...	20d	23-Dec-27	19-Jan-28
CON3-1800	Prime Coat Walls - Floor 3	15d	20-Jan-28	09-Feb-28
CON3-1900	Install Ceiling Grid - Floor 3	10d	25-Jan-28	07-Feb-28
CON3-2000	Install Ceiling Fixtures - GRD's - Floor 3	15d	08-Feb-28	28-Feb-28
CON3-2200	Finish Paint - Floor 3	15d	10-Feb-28	01-Mar-28
CON3-2300	Install MEP Devices & Trim - Floor 3	20d	02-Mar-28	29-Mar-28

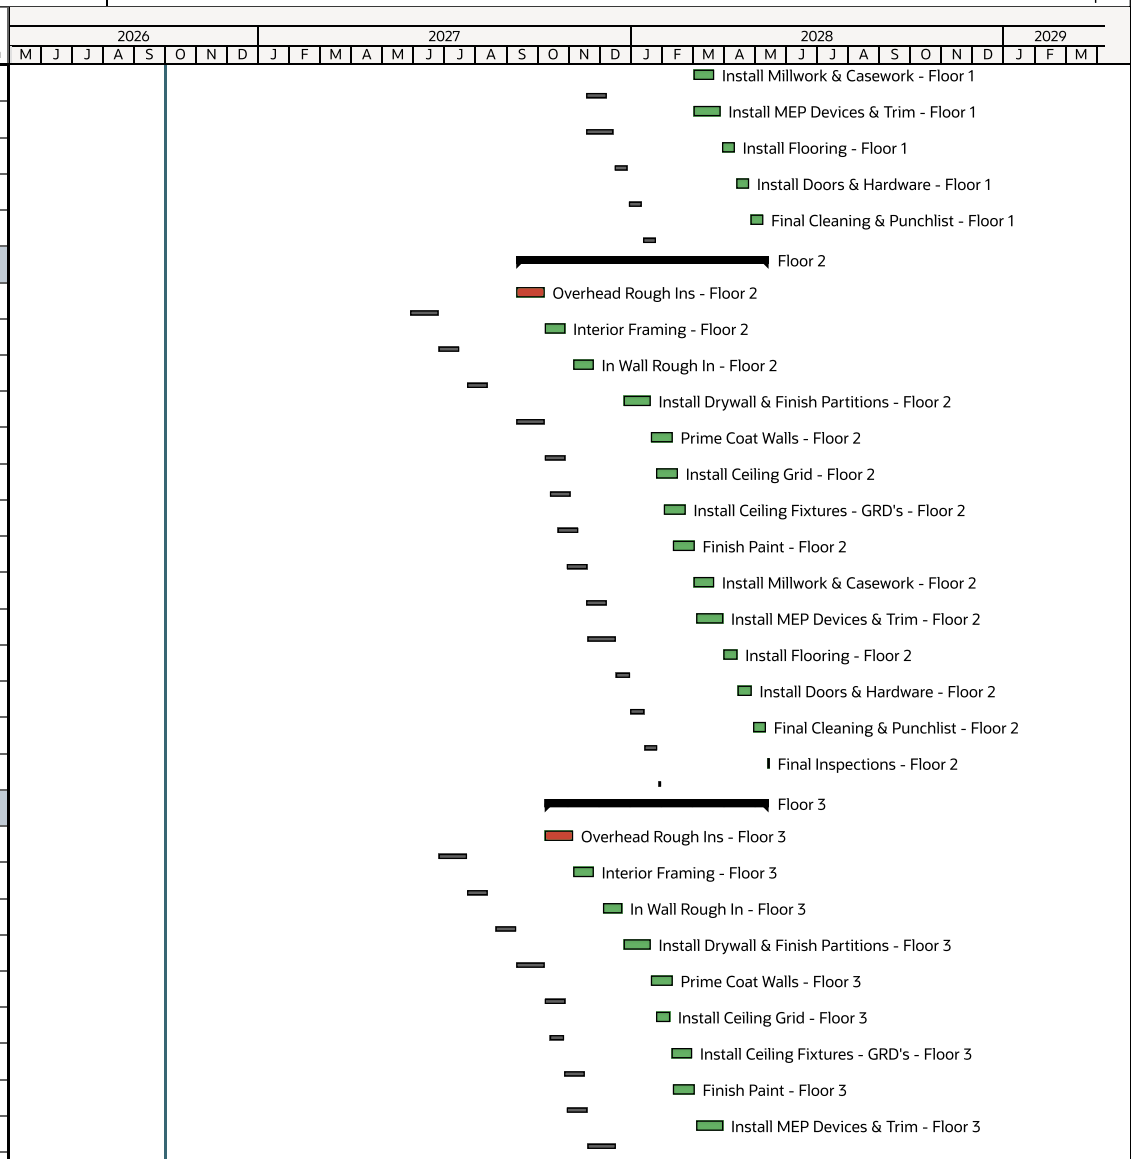

Current
Progress
Critical
Current Baseline
Original Baseline
Milestones
Summary


Willow Grove Annex Renovation Project

SKANSKA

Print Date: 19-Oct-26

Data Date: 30-Sep-26

ID	Name	Remaining Duration	Start	Finish
CON3-2100	Install Millwork & Casework - Floor 3	15d	07-Mar-28	27-Mar-28
CON3-2400	Install Flooring - Floor 3	10d	30-Mar-28	12-Apr-28
CON3-2500	Install Doors & Hardware - Floor 3	10d	13-Apr-28	26-Apr-28
CON3-2600	Final Cleaning & Punchlist - Floor 3	10d	27-Apr-28	10-May-28
CON3-2700	Final Inspections - Floor 3	2d	11-May-28	12-May-28
Floor 4		152d	04-Nov-27	02-Jun-28
CON4-1200	Overhead Rough Ins - Floor 4	20d	04-Nov-27	01-Dec-27
CON4-1400	Interior Framing - Floor 4	15d	02-Dec-27	22-Dec-27
CON4-1500	In Wall Rough In - Floor 4	15d	30-Dec-27	19-Jan-28
CON4-1600	Install Drywall & Finish Partitions - Fl...	20d	13-Jan-28	09-Feb-28
CON4-1800	Prime Coat Walls - Floor 4	15d	10-Feb-28	01-Mar-28
CON4-2200	Finish Paint - Floor 4	15d	02-Mar-28	22-Mar-28
CON4-1900	Install Ceiling Grid - Floor 4	10d	02-Mar-28	15-Mar-28
CON4-2000	Install Ceiling Fixtures - GRD's - Floor 4	15d	09-Mar-28	29-Mar-28
CON4-2300	Install MEP Devices & Trim - Floor 4	20d	23-Mar-28	19-Apr-28
CON4-2100	Install Millwork & Casework - Floor 4	15d	30-Mar-28	19-Apr-28
CON4-2400	Install Flooring - Floor 4	10d	20-Apr-28	03-May-28
CON4-2500	Install Doors & Hardware - Floor 4	10d	04-May-28	17-May-28
CON4-2600	Final Cleaning & Punchlist - Floor 4	10d	18-May-28	31-May-28
CON4-2700	Final Inspections - Floor 4	2d	01-Jun-28	02-Jun-28

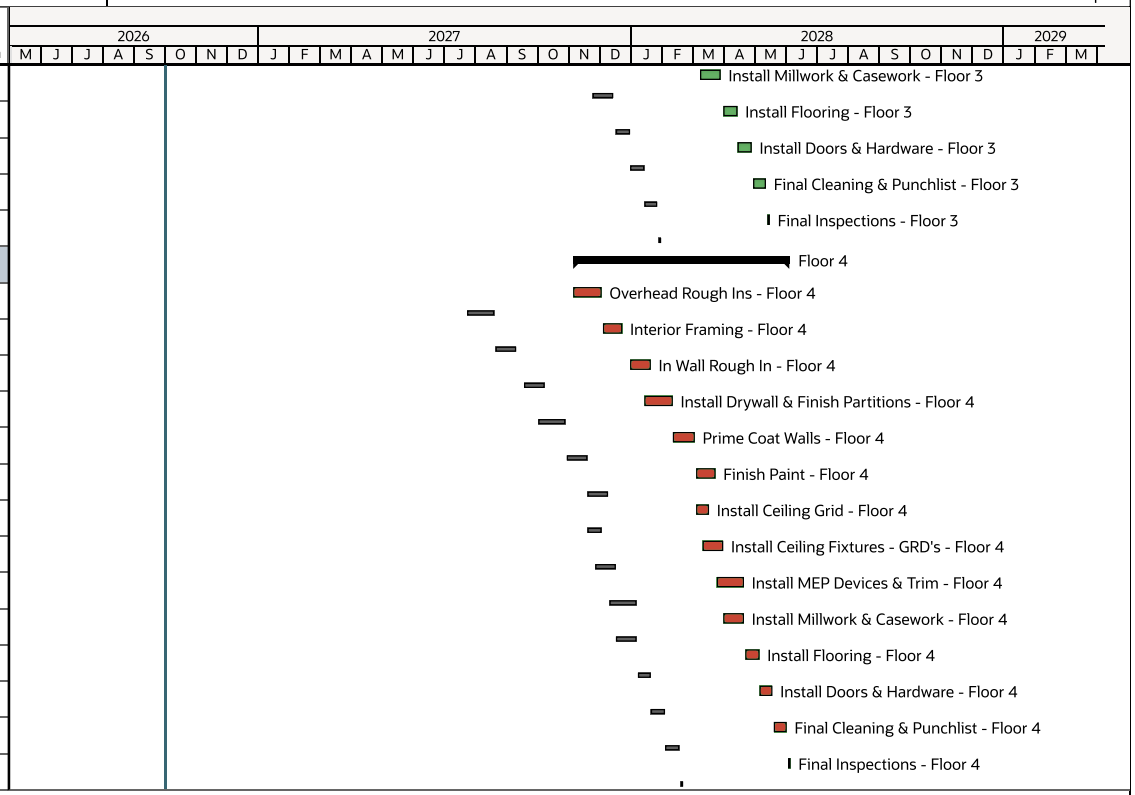

Current
Progress
Critical
Current Baseline
Original Baseline
Milestones
Summary

Willow Grove Annex Renovation Project

SKANSKA
